

Project:

**SUPPLY, INSTALLATION, TESTING, COMMISSIONING OF 500 KVA
STAND BY DG SETS**

AT

IBA BOYS HOSTEL

MINUTES OF MEETING HELD ON 10TH MARCH, 2022

A meeting was held on 10th March 2022 on above referred subject at 04.00 PM
Venue Board Room Project Department at IBA Karachi Main Campus.

The following attended the meeting.

From IBA

1. Mr. M. Nasim ul Haque Malik, Sr. Manager Planning & Contracts, IBA Karachi
2. Mr. Ishfaqe Ahmed, Assistant Engineer Electrical, IBA Karachi
3. Mr. Ashar Hussain, Junior Project Engineer Civil, IBA Karachi


Representatives:

1. Mr. Syed Azam Hussain, Manager Sales – Energy Solutions (Pvt.) Ltd
2. Mr. Bilal Uddin Siddiqui, Senior Application Engineer – Jaffer Brothers (Pvt.) Ltd
3. Mr. Nisar Ahmed, Sr. Project Engineer – Greaves Pakistan (Pvt.) Ltd
4. Mr. Siraj ul Islam, Manager Project – W.S Global

Following were the queries discussed during the meeting.

| Sr. No. | Discussions | Replies / Actions |
|--------------------|---|---|
| 1 | As discussed, the Power cable shall be 2x4C-185 sq.mm Cu. PVC/PVC, armored insulated cables . | For information only. |
| 2 | The length of control cable shall be approx. 100 feet from DG set to main Panel. | For information only. |
| 3 | As pointed out by one of the participants that there shall be no need of spring | Item # 05 to be deleted from the scope. |

| | | |
|---|---|--|
| | isolators for ground mount 500KVA genset. | |
| 4 | The vendor required earthing drawing to bid the quote as per requirement of client. | Attached for your necessary action. |
| 5 | Earthing Material testing to be performed before the commencement of work. | The vendor to submit the necessary test reports and ensure the copper rod. |
| 6 | The vendor to submit proposed civil pad structural drawing on later stage and get approval from client. | For information only. |
| 7 | As discussed with participants that bid shall submit in PKR and there will be no escalation to be claimed by vendor in later stage. | For information only. |

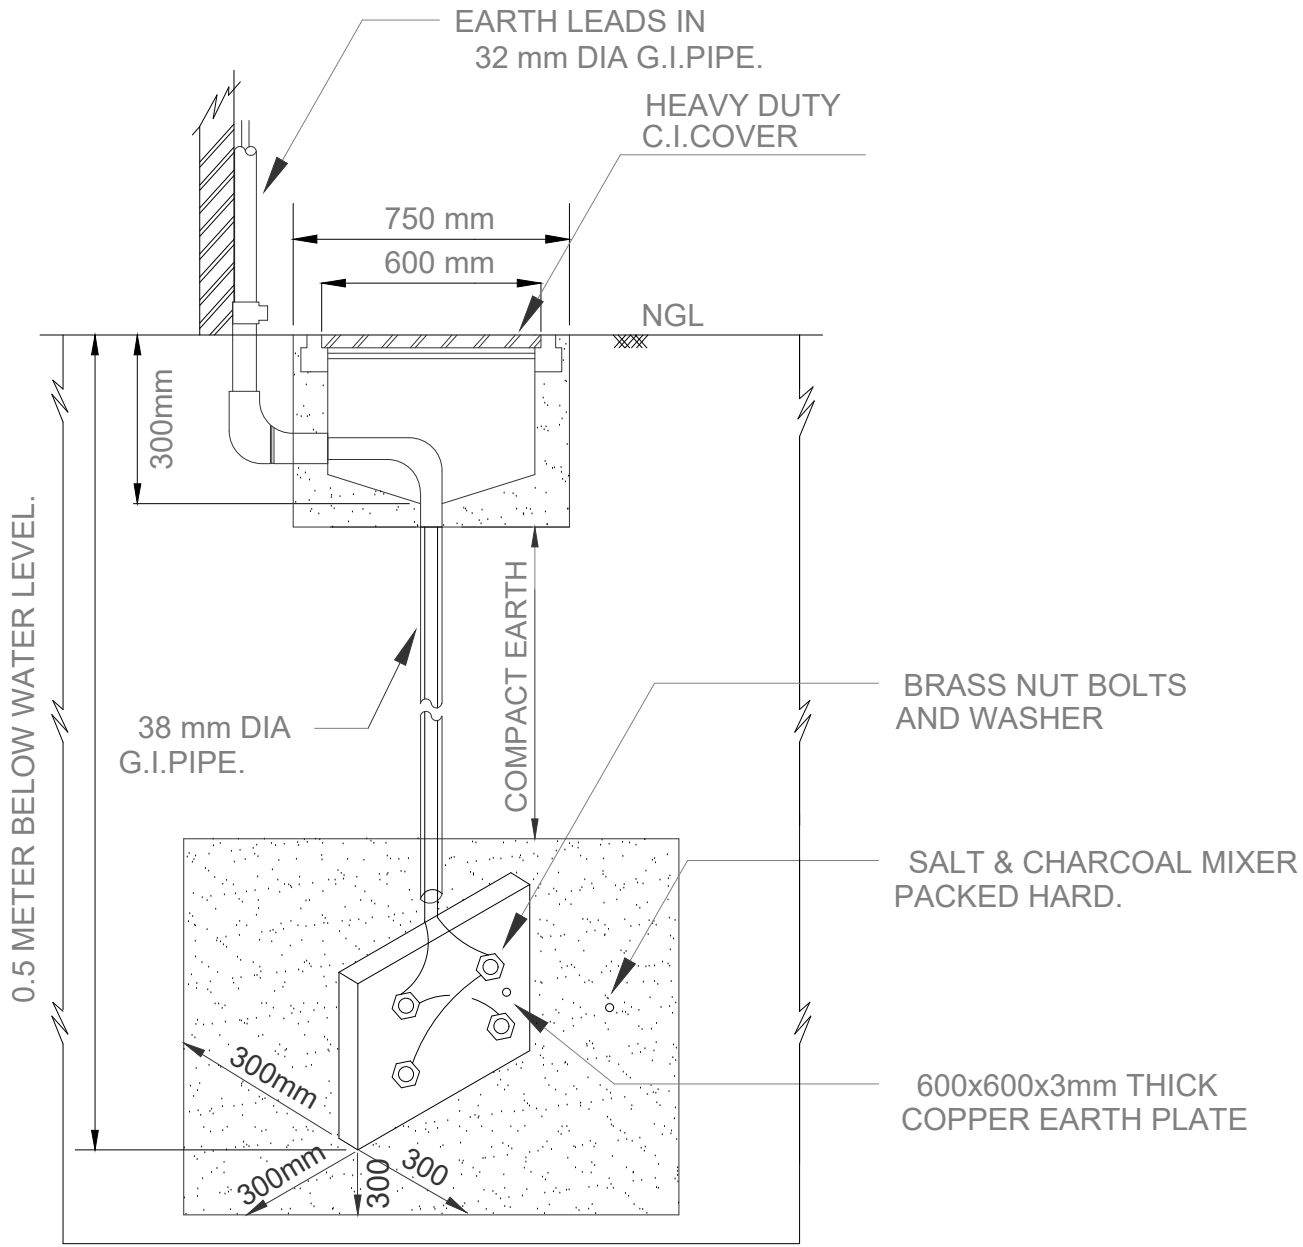

EARTHING DETAIL

Note: Earthing Results should achieve as per BOQ.

| | | | |
|------|-----------------|-----|-------|
| OO | TANDER-DRAWINGS | I.A | 03-22 |
| REV. | DESCRIPTION: | BY: | DATE: |

GENERAL NOTES

PROJECT NAME:
BOYS HOSTEL - IBA KARACHI

DRAWING TITLE:
EARTHING LAYOUT

DRAWN BY:
I.A

CHECKED BY:
I.A

APPROVED BY:
N.M

DATE:
01/2022

BY:
500 KVA GENSETS FOR BOYS HOSTEL

PROJECT NO:
GH-01


SCALE:
N.T.S

SHEET SIZE:
A0

DRAWING NO:
EAR-01

SHEET NO:
0 OF 0

REVISION:
00



UNIT:
FEET
